



# Plan Summary

## October 2016 - Review Update

2016/17

# Outcomes by April 2017



- Monmouthshire County Council still **actively partnering us** in the delivery of Magor and Undy Walkway station
- We are **certain** that we will achieve the aim of a station for Magor and Undy
- Residents understand that MAGOR has **helped establish the 3 Fields Community Trust** to deliver a community centre which is potentially linked to a new station
- Rail Industry is **now supportive** about Magor and Undy Walkway station
- Welsh Government is supportive of and **promoting our community led initiative**
- The press and **increasingly the national media** are taking an interest in our progress
- The **GRIP 3 process is funded** and has been **completed**
- **The GRIP 4 process has been commissioned**
- People are still very supportive of MAGOR and its campaign for a new station and improved rail services
- **People understand concept of a Walkway and are contributing ideas to overcome the 'parking risk'**
- **People aware of MAGOR's input to the wider transport improvements for Severnside**
- Still **financially secure** to maintain progress


# Target Milestones 2016/17



Lead person shown in red

- **A** - GRIP 2 study assessed (with MM and NR) and draft plan produced for commissioning the GRIP 3 study (option selection) – June 2016 (TH/PT/MR) - **Completed**
- **B** - Data gathered that will contribute to GRIP3 development July 2016 (TH/PT/MR) - **Completed**
- **C** - Met Welsh Government reps and support obtained – July 2016 (TH/PT) – **Re-planned**
- **D** - GRIP 3 potential suppliers identified - June 2016 (TH/PT) - **Completed**
- **E** - GRIP 3 supplier identified and quote obtained - July 2016 (TH/PT) - **Completed**
- **F** - UWE student report delivered to contribute to GRIP process August 2016 (TH/MR) - **Completed**
- **G** - Secured sufficient funds to initiate GRIP 3 process – End of September 2016 (JW/PW/TH/PT) – **Re-planned**
- **H** - GRIP 3 report delivered – December 2016 (TH/PT) – **Re-planned**
- **I** - Data gathered that will contribute to GRIP 4 – January 2017 (PT) – **Included in GRIP 3**
- **J** - GRIP 4 Initiated – March 2017 (TH/PT) – **To be reviewed**
- **K** - '3 Fields Site' under development and MAGOR hold a seat in the 'consortium' management group - June 2016 (PW/PT) – **Completed and ongoing (outside of MAGOR project)**
- **L** - Accessible Transport Plan produced by Severnside Group and supported by MAGOR group – November 2016 (PT) – **Re-planned (dependent on MCC Corporate Governance Proposals)**

# Target Milestones 2016/17

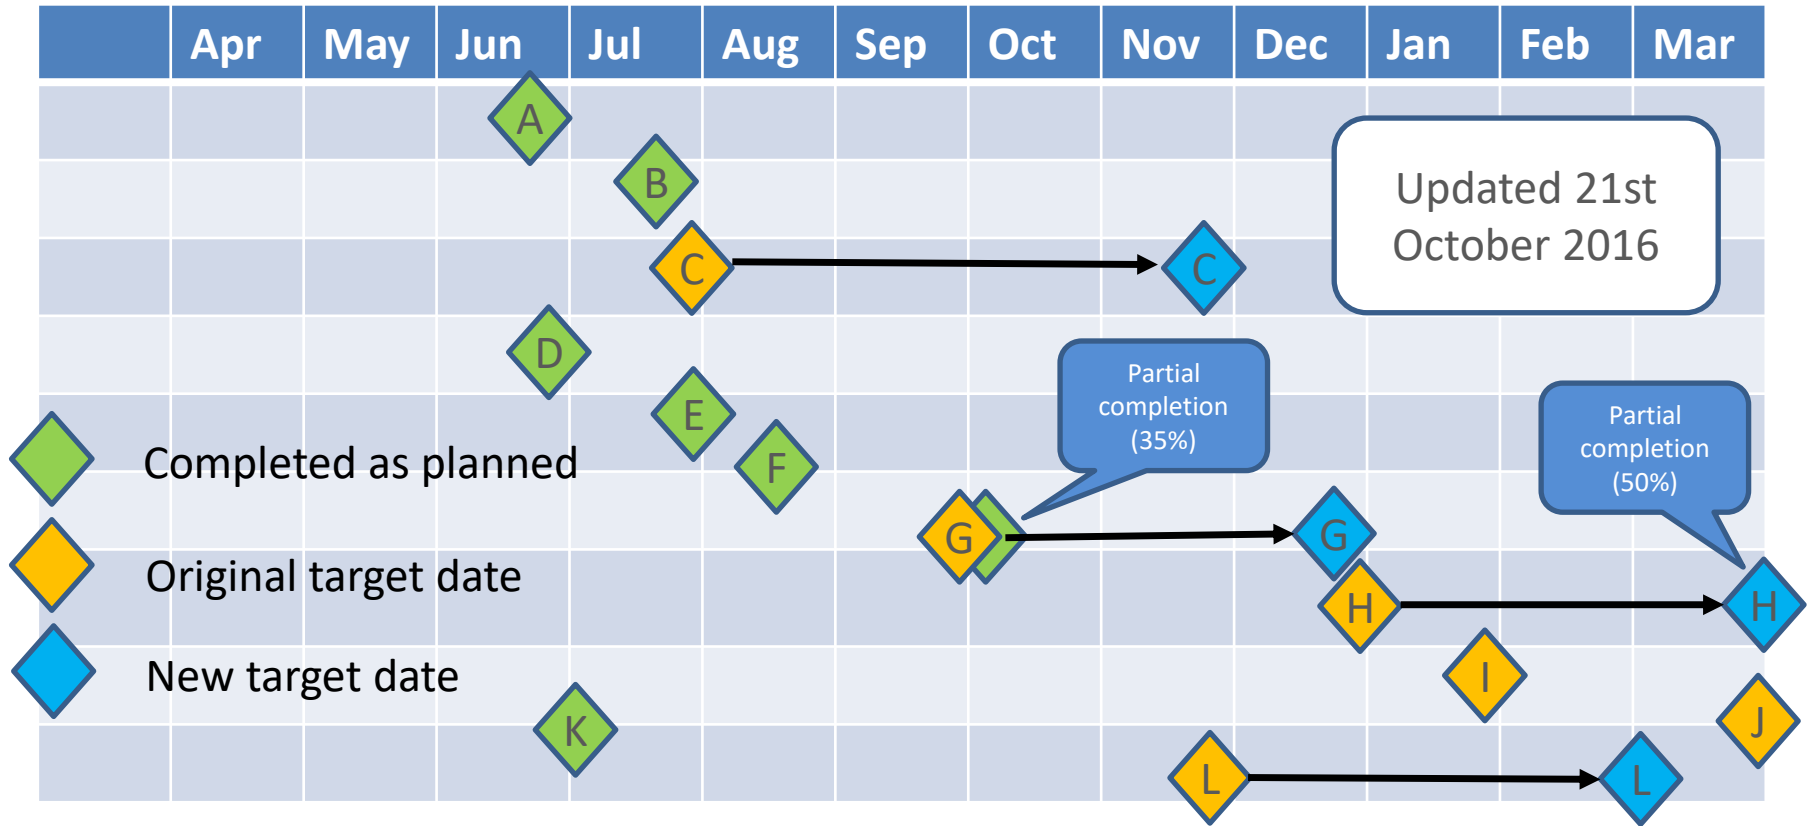

A – GRIP2 Assessed

B – Data Gathered

C – WG met/support

D – GRIP 3 Suppliers found

E – Supplier agreed

F – UWE report

G – Funding in place

H – GRIP 3 delivered

I – Data gathered

J – GRIP4 initiated

K – 3FS Consortium

L – Accessible Transport
